


Skyhaven Airport Construct, Mark, Light & Sign Taxiway 'A'

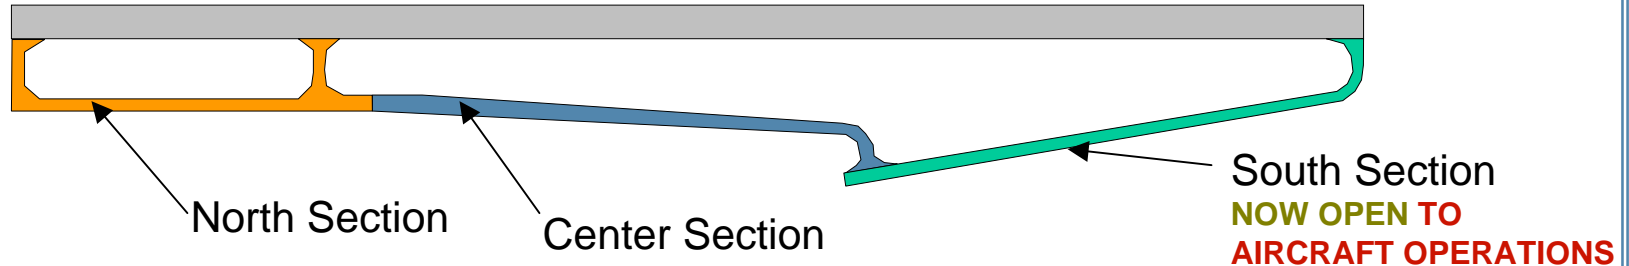

PROJECT UPDATE

November 19, 2007

The construction work to the south section of Taxiway 'A' was substantially completed today, November 19, 2007. In the spring, after the snowplowing season, the contractor will return to this section of pavement to place the 2nd coat of taxiway paint markings, relocate the easterly edge of taxiway lights, and hydroseed the easterly taxiway shoulder. In the meantime, the project area will be stabilized for the winter and cleanup activities will be wrapping up shortly.

Construction efforts for the North Section of Taxiway 'A' may start as early as the week of January 21st.

NHDOT is committed to providing the airport tenants and visitors with the latest information on this project.

To receive e-mail updates on this project's progress or to ask questions about the project, please call (603) 271-2552 or e-mail cniewola@dot.state.nh.us.

For *immediate* project concerns, please contact Ossipee Valley Aviation and the information will be relayed to the appropriate parties.
