


Skyhaven Airport Construct, Mark, Light & Sign Taxiway 'A'

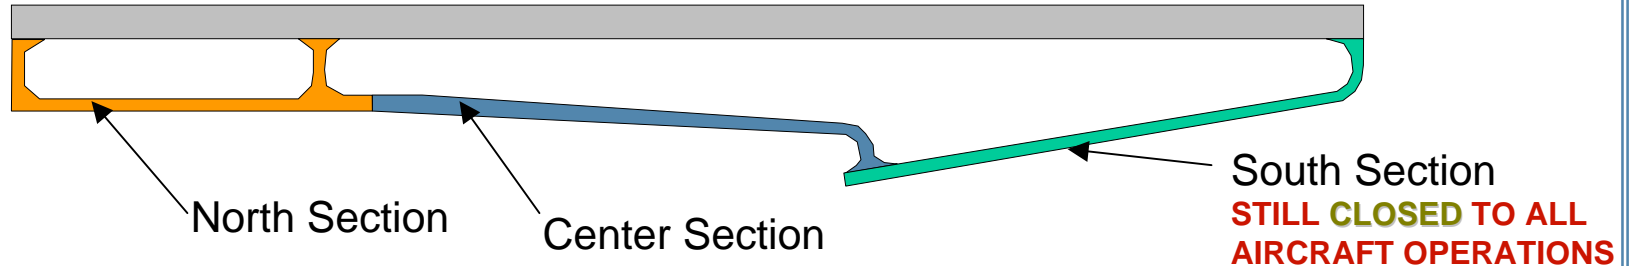

PROJECT UPDATE November 2, 2007

The work on the South Section of Taxiway 'A' remains on schedule. Paving the first test strip occurred Wednesday, October 31st. A second pavement test strip will likely be paved on Monday, November 5th or Tuesday, November 6th. Full paving production is anticipated for Wednesday, November 7th through Friday, November 9th, weather permitting. While the South Section of Taxiway 'A' remains **closed** during this paving, the FBO maintenance hangar will be accessible on a prior notice required basis. The taxiway will reopen to all traffic during the week of November 12th after the taxiway paint has been applied.

NHDOT is committed to providing the airport tenants and visitors with the latest information on this project.

To receive e-mail updates on this project's progress or to ask questions about the project, please call (603) 271-2552 or e-mail cniewola@dot.state.nh.us.

For *immediate* project concerns, please contact Ossipee Valley Aviation and the information will be relayed to the appropriate parties.
